


Projected Project Schedule

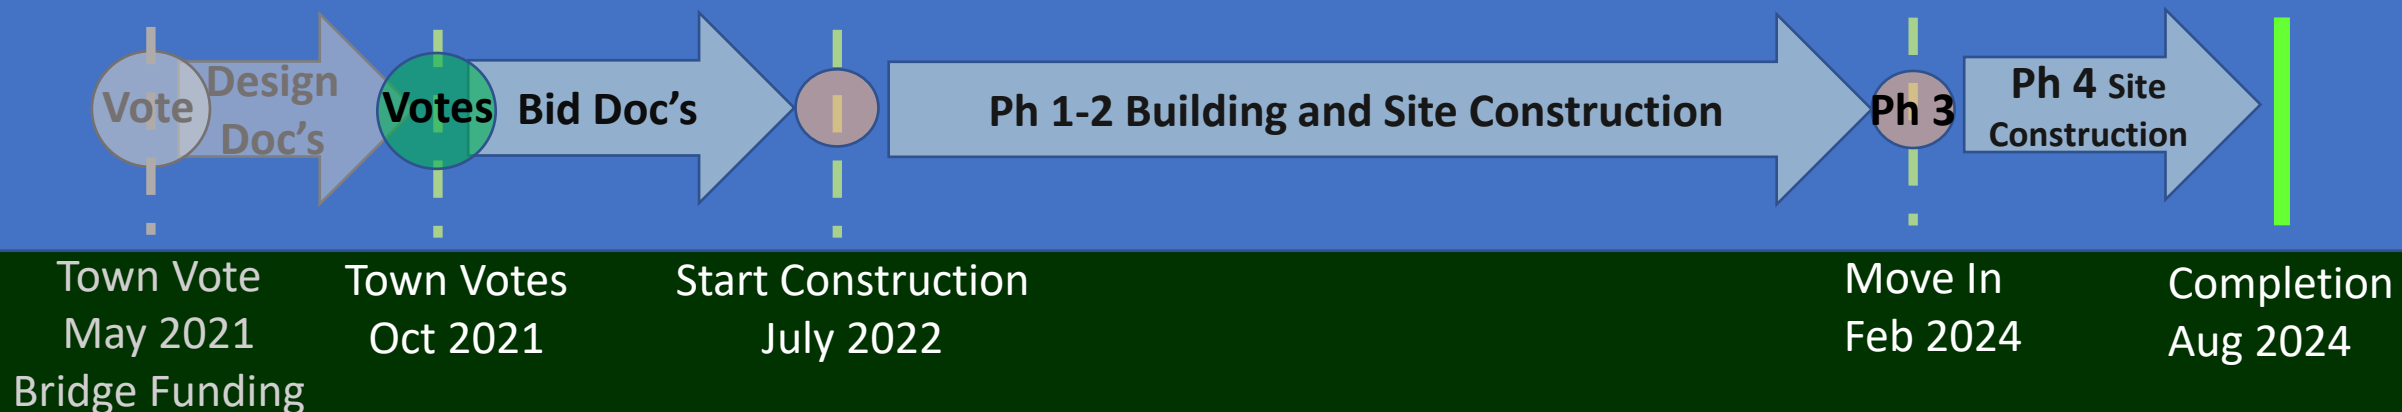


Votes and Bid Document Prep: Spring 2021- Spring 2022

- Feb 2021: Submit SD package to MSBA
- Apr 2021: MSBA SD Vote
- May Town Vote: Bridge Funding DD Phase
- June-Sept 2021: 4 months of Design Development
- Oct 18 Town Meeting and Oct 26 Town Vote: Full Project
- Nov 2021-May 2022: 7 months of Construction Documents

Construction: Summer 2022- Summer 2024

- June-July: 2 months bidding
- July 2022-Feb 2024: 19 months building construction
- Feb 2024: Move into new school
- April 2024-Aug 2024: Demo existing building – complete remaining site work

Construction Document Phase: Work Plan

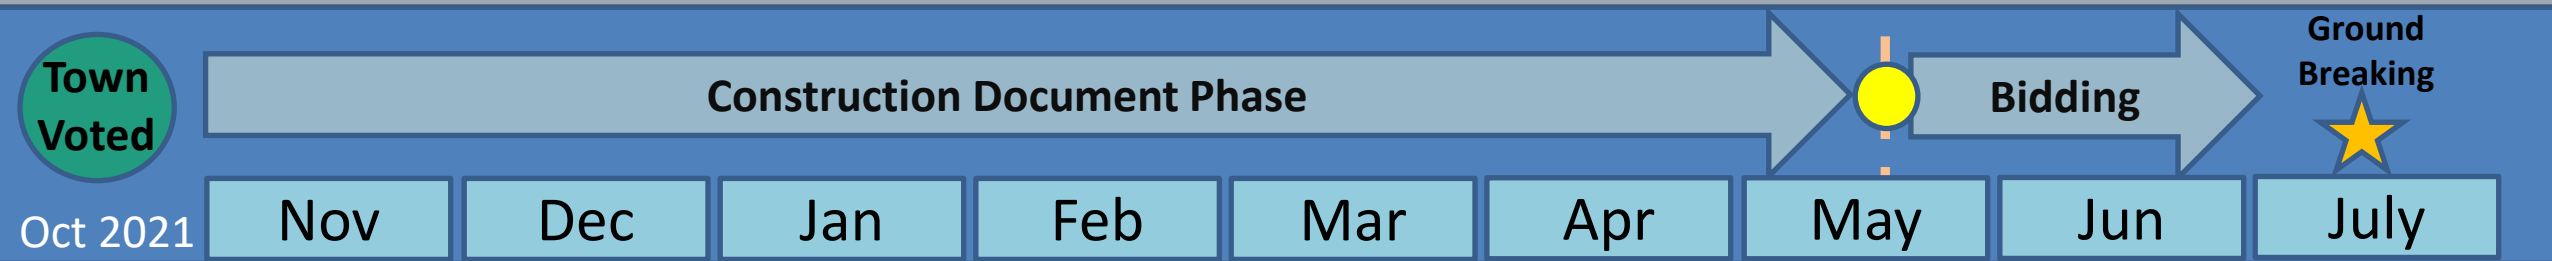

Three Month Look Ahead

November

- Nov 3: Test Pits
- Nov 5: SBC authorizes CD phase
- TBD: Two Aesthetic + Design Meetings:
 - Terracotta (propose Nov 17th)
 - Canopy + Interiors Review (propose Dec 1)
- Nov 30: Planning Board Cont. Hearing

December

- Dec 3: SBC Meeting- vote on A+D recommendations
- Dec 8: Conservation Committee Cont. Hearing
- TBD: Aesthetic + Design Meeting
 - a. Interiors Finishes Review (propose Dec 8)
- Dec 21: Submit 60% CD to estimators
- Dec 22: Begin GC + Sub Prequal RFQ

January

- Jan 7: SBC Meeting (*propose moving to Jan 21*)
- Jan 11-12: Room Data Sheet Review and sign off
- Jan 12 Receive 60% cost estimates
- Propose Jan 21 in lieu of Jan 7: SBC Meeting authorize 60% CD submission to MSBA*
- Jan 24: Submit 60% CD to MSBA
